

# PROJECT STATUS UPDATE

## Farmington Public Schools

Bid Package # 7

2020 Bond Issue – Maxfield Education Center & STEAM Academy

# Maxfield Education Center – Project Description

## Project Description:

This project involves selective interior architectural, mechanical, electrical, and plumbing renovations throughout the Maxfield Education Center building. As well as selective exterior site improvements.





# Maxfield Education Center – Project Overview

## Project Overview:

Existing flooring has been demoed and new carpeting is currently being installed in the I.T. area.





# Maxfield Education Center – Project Overview

## Project Overview:

New exterior FRP doors have been installed in selective areas of the building.







# Maxfield Education Center – Project Overview

## Project Overview:

Selective painting is ongoing throughout the building.

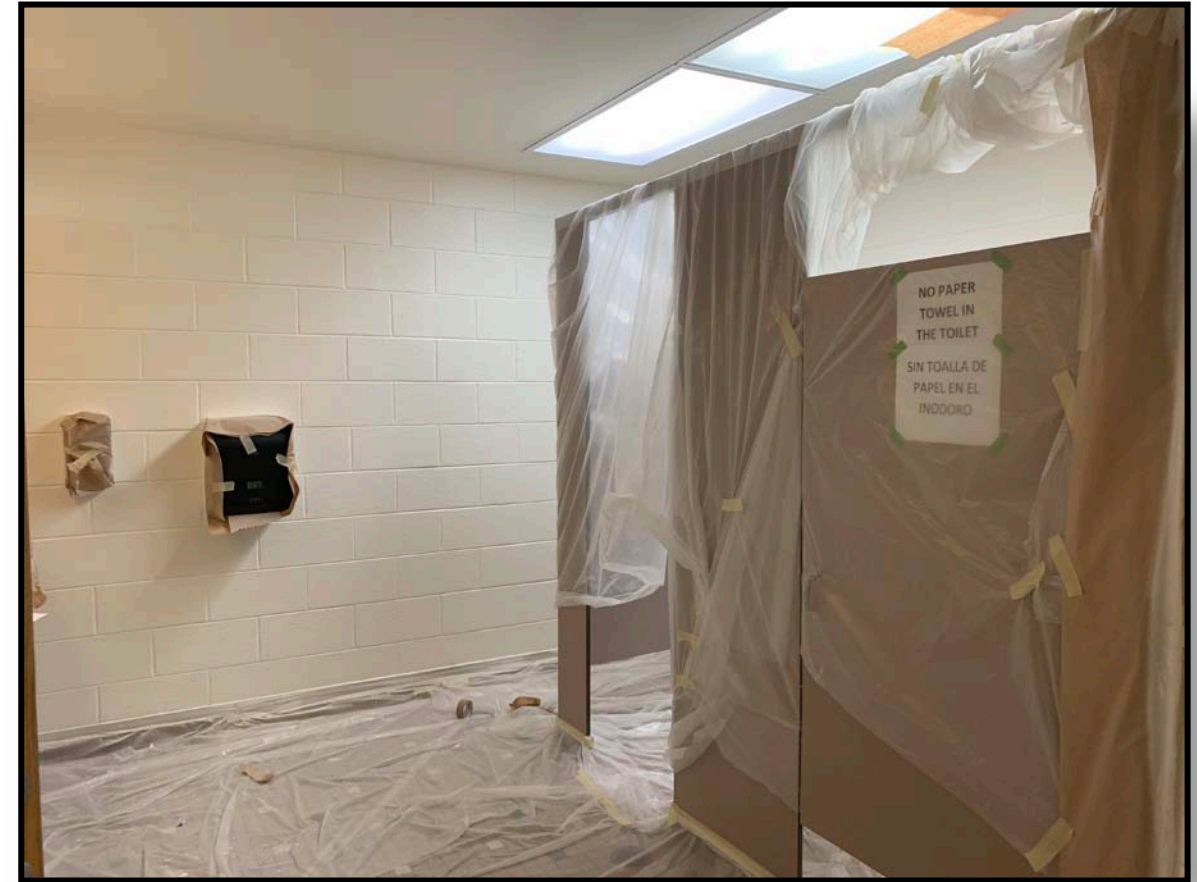

# Maxfield Education Center – Three Week Look Ahead

PROJECT NAME		Farm. Bid Pack #7																									
LOCATION		MEC																									
Three Week Look Ahead		2/20/2023																									
Week of 02/20/2023 through 03/12/2023																											
		Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun					
TASK		20	21	22	23	24	25	26	27	28	01	02	03	04	05	06	07	08	09	10	11	12					
Interior	Contractor																						Notes				
Brick Infill above CUH #4	DC Byers	X																									
Painting throughout Main Area Interior	Seven Brothers		X	X	X	X			X	X	X																
Demo/framing of New Smoke Dampers	A.M. Higley								X	X	X																
Floor Demo Room # 118 & 120 I.T. Area	DKI	X																									
Acoustical Ceiling Installation in Main Area	A.M. Higley											X	X			X	X										
Duct, Ceiling Wall Painting in I.T. Area	Seven Brothers	X	X	X																							
Ceiling Tile Installation in I.T. Area	A.M. Higley		X	X																							
Cleaning I.T. Area	McCarthy & Smith				X																						
Smoke Damper Framing in Soffits	A.M. Higley								X	X	X																
Exterior Aluminum Frame Door Installation	Trenko Glass	X	X	X																							
Wiring Porta John	Aces Electric									X	X												Site Delivery 2/27 or 2/28				
Cabinet Unit Heaters & Misc. Valve Installation	Systemp/Aces	X	X	X																							
Planter Area Brick Re-Work and Pedestals	DC Byers								X	X	X	X	X			X	X	X	X	X							



March 02, 2023

