

PROJECT STATUS UPDATE

Farmington Public Schools

Bid Package # 16

2020 Bond Issue - Visions Unlimited



Visions Unlimited – Project Description

Project Description:


The Visions Unlimited project includes demolition and re-work throughout the interior and exterior of the old Farmington Central High School building (in order to provide a new space for the Visions Unlimited program).



Visions Unlimited – Project Overview

Project Overview:


Selective new walls are being taped, sanded and primed throughout the building.



Visions Unlimited – Project Overview

Project Overview:


New gypsum board ceilings are being installed in selective rooms throughout the building.




Visions Unlimited – Project Overview

Project Overview:

New CMU walls have been installed in preparation for a new janitors closet.

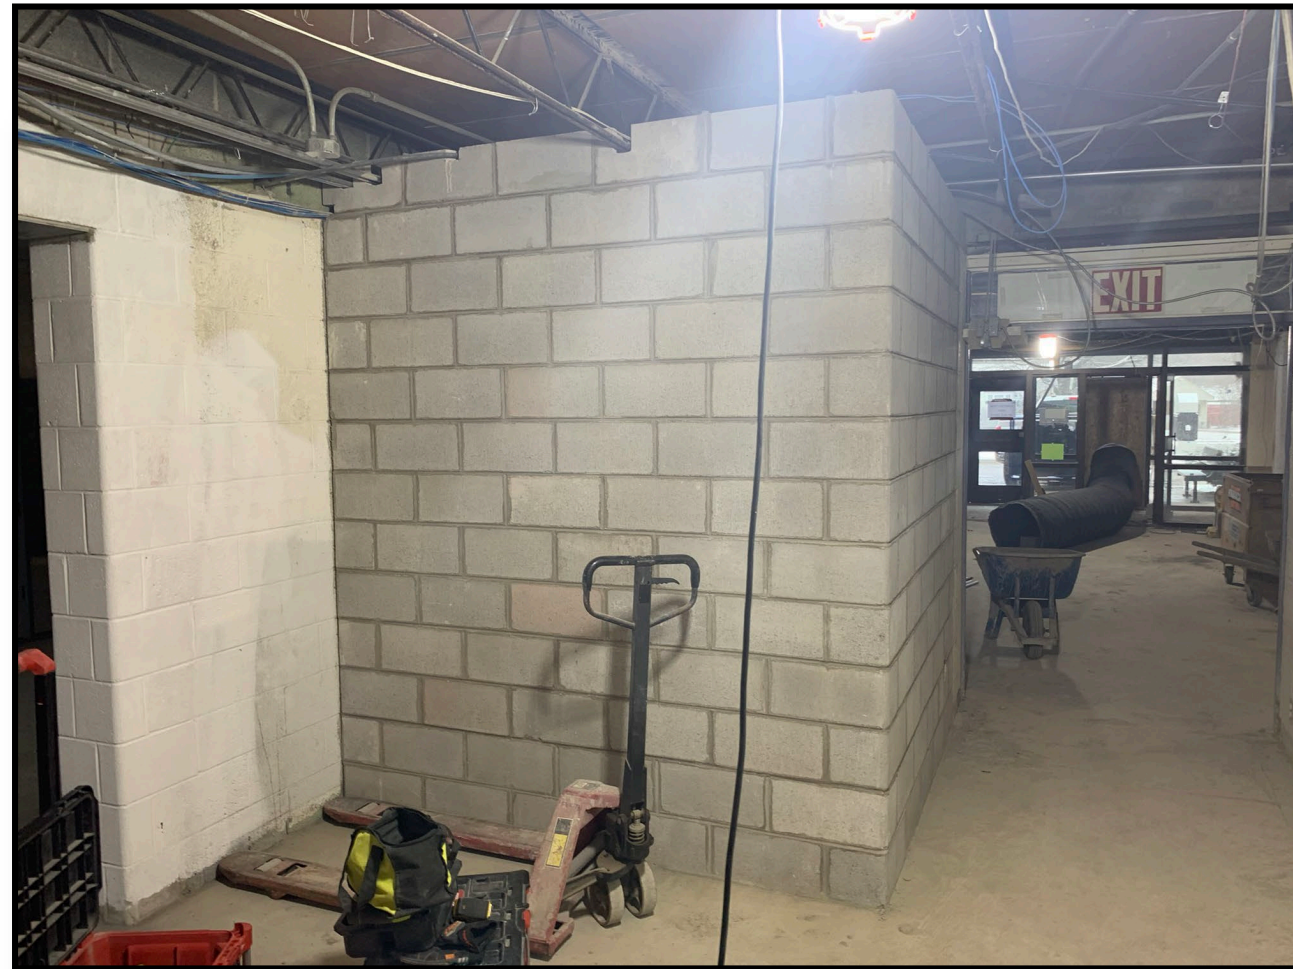

Visions Unlimited – Three Week Look Ahead

		FPS 2021 Bid Pack 16: Visions Unlimited																								Period Start: 3/20/2023	
		3-WEEK LOOK-AHEAD SCHEDULE																								Period End: 4/9/2023	
																										Prepared By: Jeff Robinette	
																										Page: 1 of 1	
Activity Description	Contractor	Scheduled Start	Week 1 3/20/2023							Week 2 3/27/2023							Week 3 4/3/2023							Scheduled Finish	Remarks		
			20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9				
			M	T	W	Th	F	S	S	M	T	W	Th	F	S	S	M	T	W	Th	F	S	S				
Visions Unlimited																											
Electrcal Rough - Area A, B North Quad	Max Elec	12/27/23	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			4/7/23			
Mud/Tape/Sand Drywall Classroom Entries	AM Higley	2/20/23	X	X	X	X	X																	3/24/23	After Approval of Elec Inspection		
Drywall - Area A, B Classrooms	AM Higley	4/3/23															X	X	X	X	X			2/1/23			
Install/Pipe Unit Ventilators	Contrast Mech	3/20/23	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			4/14/23			
Plumb For Classroom Fixtures	Contrast Mech	3/20/23	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			3/1/23			
Install Fire Pro Main and components	Absolute Fire Pro	2/6/23	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			4/14/23	Area B, S/W Quad needs to be completed 3/31.		
Install Drywall Ceilings	AM Higley	4/10/23															X	X	X	X	X			4/28/23			
Ceiling Grid Install	ACP	4/3/23	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			5/5/23			
Roofing	Superior Services	4/3/23															X	X	X	X	X			4/14/23			
Paint - Classroom Walls and Ceilings	DTS Contracting	4/19/23																						5/10/23			
Kitchen Quarry Tile Install	DF Floors	4/3/23															X	X	X	X	X			4/14/23			
Tile Classroom Bathrooms	DF Floors	4/17/23																						5/26/23			
Soil Erosion Measures	Cortis Bros	3/23/23				X	X																	3/24/23			
Asphalt Demolition	Nagle Paving	4/3/23															X	X	X	X	X			4/11/23			
