

PROJECT STATUS UPDATE

Farmington Public Schools

Bid Package # 8

2020 Bond Issue – North Farmington High School



North Farmington High School

Project Description:


The North Farmington High School project includes selective architectural, mechanical, electrical and plumbing renovations throughout the interior of the building. As well as, a substantial renovation to the building's kitchen.



North Farmington High School

Project Overview:

- CMU wall construction is nearly complete in the kitchen.

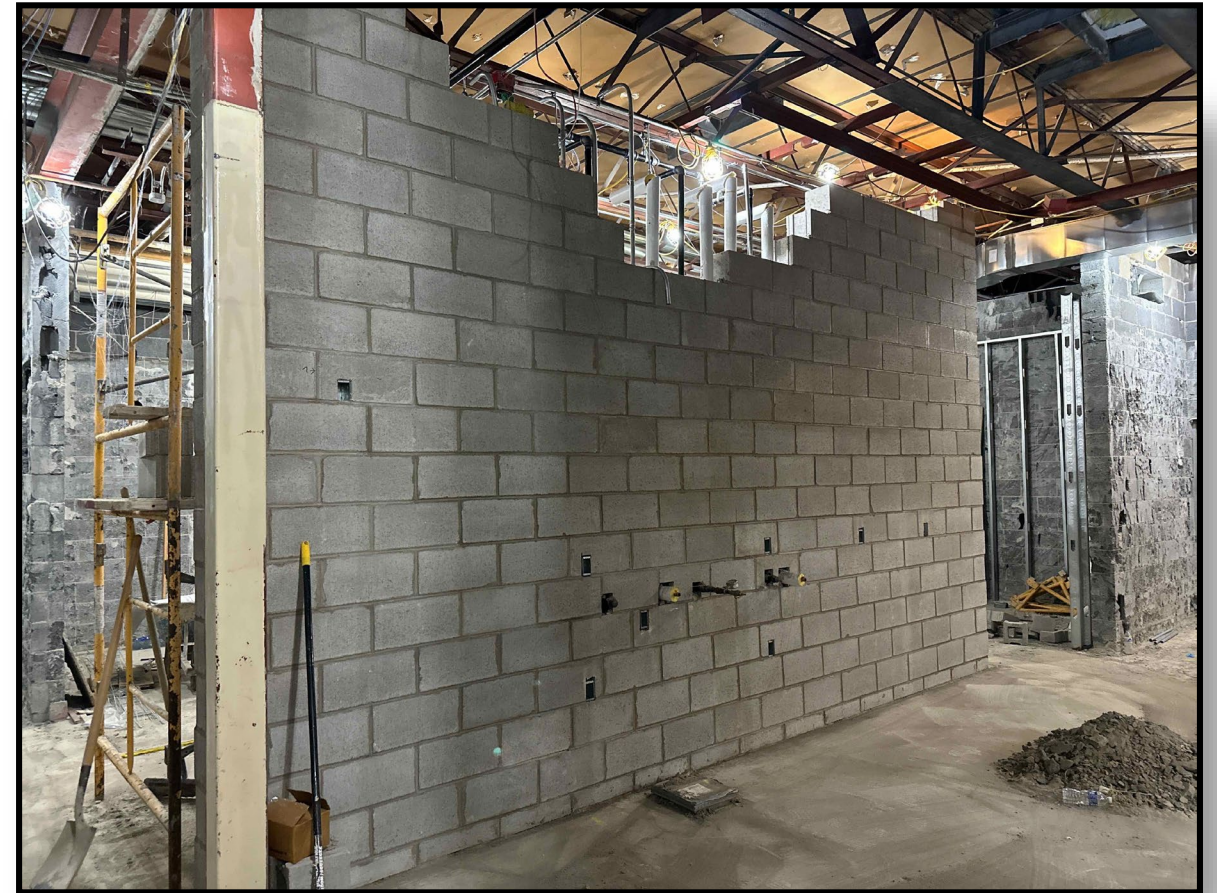


North Farmington High School

Project Overview:

- CMU wall construction is nearly complete in the kitchen.



North Farmington High School – Three Week Look Ahead

3-Week Look Ahead Schedule																													
		<div>Farmington Public Schools</div> <div>North Farmington High School</div> <div>3-Week Look Ahead Schedule</div>																								<div>Period Start: 5/15/2023</div> <div>Period End: 6/4/2023</div> <div>Prepared By: Jose Jimenez</div>			
Activity Description	Contractor	Week 8 5/15/2023							Week 9 5/22/2023							Week 10 5/29/2023							Notes						
		15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4							
		M	T	W	Th	F	S	S	M	T	W	Th	F	S	S	M	T	W	Th	F	S	S							
	Blue Star															M													
Install New Plumbing and gas lines in Kitchen area	Danboise Mech	X	X	X	X	X			X	X	X	X	X			E													
Install new duct work in kitchen area, hood prep, UV, EF, and MAU	Ecker Mechanical	X	X	X	X	X			X	X	X	X	X			M	X	X	X	X									
Pull wire in kitchen area, floor plugs, and conduits	Brenner Electric	X	X	X	X	X			X	X	X	X	X			O	X	X											
Start block wall 2nd shift	J&J	X	X	X	X	X			X	X	X	X	X			R													
	Stafford Smith															I													
Deliver all steel for block work	Zak Welding	X														A													
Start in Servery room Quarry Tile and base	D.F. Flooring								X	X	X	X	X			L	X	X	X	X									
Frame and drywall bump out walls in kitchen area	DTS			X	X	X																							
Start Demoing Pool Mechanical room	Aquatic Source															D	X	X	X	X									
	McCarthy/Smith				X											A													
																Y													
